


project phases

Phase 1 Phase 2 Phase 3





Document Path: G:\Jobs\RM150295-00 13th Ave - Illinois to Pine, Sidney\GIS\RM150295-00 13th Ave - Illinois to Pine, Sidney - Phases.mxd

Date Saved: 4/7/2021 5:04:34 PM

Phase 1 — Alley between Quince & Pine (STA. 100+88) to north side of Newton (STA 110+50)
 - Detour Route (Quince to 10th to Maple)

Phase 2 — North side of Newton (STA 118+00) to north side of Linden (STA 118+00)
 - Detour Route (Newton to 10th to King)

Phase 3 — North side of Linden (STA 118+00) to alley between US HWY 30 and Jackson (STA 126+10)
 - Detour Route (Linden to 10th to US HWY 30)

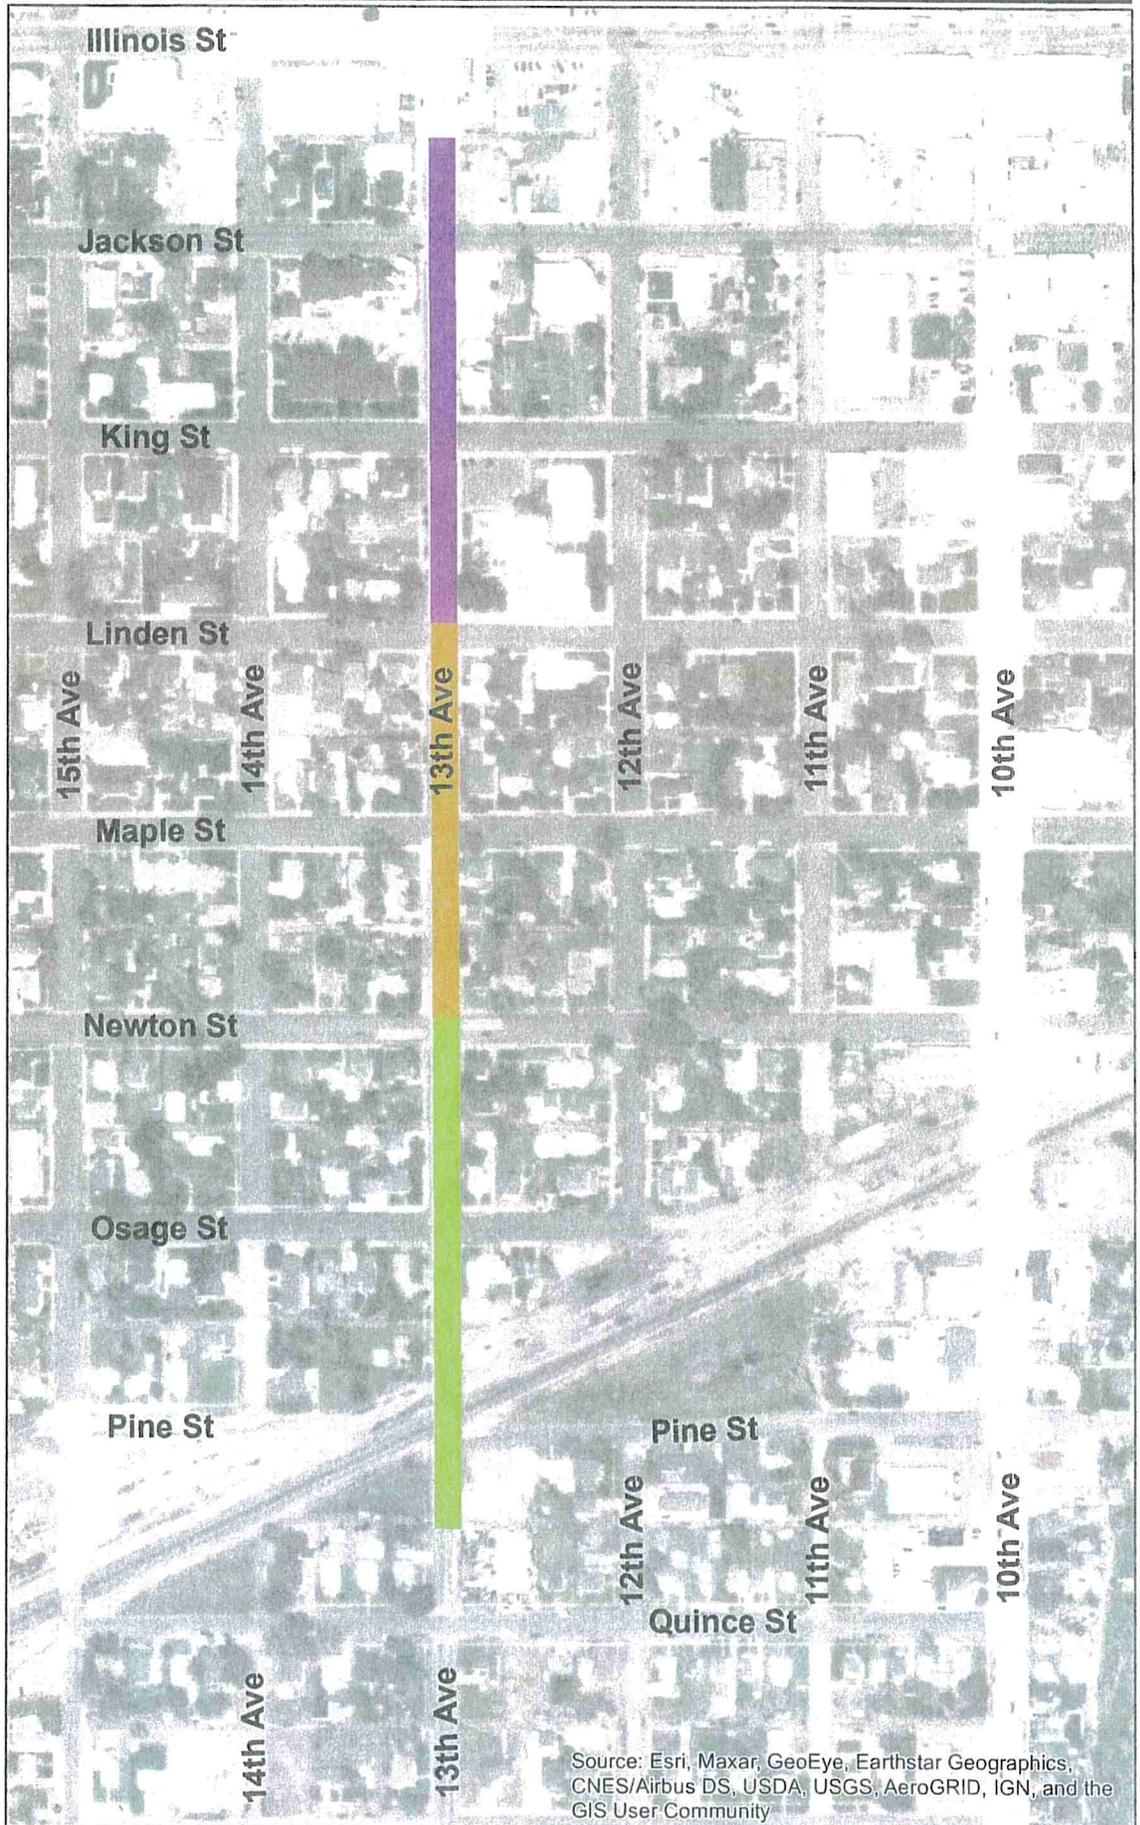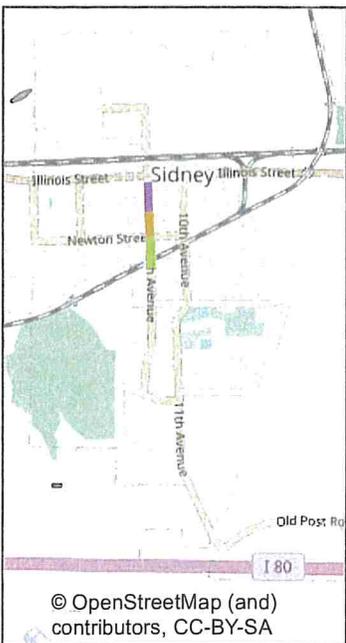

13TH AVENUE PROJECT - PUBLIC INFORMATIONAL MEETING

Welcome:

Thank you for attending the Public Informational Meeting for the City of Sidney's 13th Avenue Improvement Project. The purpose of today's meeting is to provide information on the project, present phasing, and answer questions relating to the project. Representatives from the City of Sidney, M.C. Schaff & Associates (Engineer), and Eric Reichert Insulation and Construction (Contractor) are available to answer any questions you may have regarding the project.

Project Information:

The City of Sidney is planning to reconstruct 13th Avenue between Illinois and Pine starting on April 19, 2021. The project will be constructed in three phases in order to provide access and minimize inconvenience as much as possible. It is scheduled to be completed by November 12, 2021.

Project Facts:

The 13th Avenue project will include:

- Removal and replacement of the existing pavement. The new pavement section will be the same width as before but will be constructed with 8-Inch P.C. Concrete Pavement. Curb & Gutter and Sidewalks will be replaced and will include handicap ramps at all intersections.
- A new Storm Drain system will be constructed along the project with curb inlets to collect storm water runoff and convey the storm sewer to the system on 10th Avenue. This will allow the valley gutters that cross 13th Avenue to be removed which in turn will provide a smoother ride.
- Driveway access will not be available during the construction of each phase. Door flyers of the actual date of closure will be placed prior to the start of each phase. Any sprinkler systems damaged by the construction process will be repaired by the Contractor.

Tentative Project Schedule:

April 19, 2021 – Start Construction

April 19, 2021 through July 2, 2021 – Phase 1 Construction

July 6, 2021 through September 3, 2021 – Phase 2 Construction

September 3, 2021 through November 12, 2021 – Phase 3 Construction

A phasing plan is attached.

Project Contacts:

David Scott
City Manager
City of Sidney
1115 13th Avenue
Sidney, NE 69162
308.254.5300
citymanager@cityofsidney.org

Don Dye
Project Manager
M.C. Schaff & Associates
818 S. Beltline Hwy E
Scottsbluff, NE 69361
308.635.1926
ddye@mcschaff.com

If you would like to receive updates as the project progresses, please leave your email address on the sign in sheet or send a request to Don Dye at the email address above.
